




**City of
Santa Clara**
The Center of What's Possible

Additional Youth Soccer Fields & Athletic Facilities Project

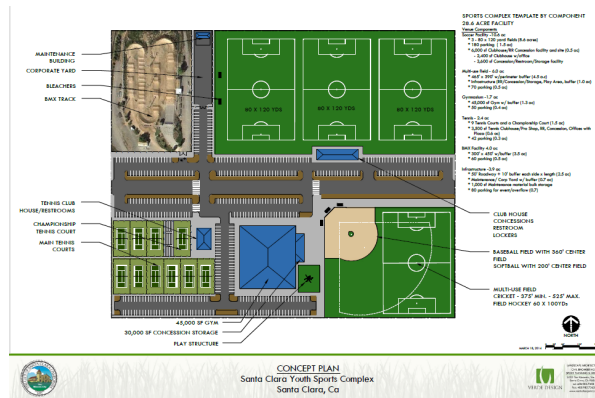

Project Timeline	Status	Date
Council adopts goal to “Enhance Community Sports & Recreational Assets”	Completed	September 13, 2013
Council approves Youth Sports Complex Needs Assessment and Site Feasibility Study	Completed	November 12, 2013
Parks & Recreation Commission recommends Council prioritize development of additional soccer fields and athletic amenities in the Youth Sports Complex Concept Plan	Completed	March 25, 2014
Council establishes Capital Improvement Project #3177 and allocates \$2mm (of \$10mm)	Completed	March 25, 2014
Council Ad Hoc Committee reviews access to Youth Soccer Park, soccer ready alternative facilities, potential park sites for installation of new soccer and athletic facilities, mitigation measures to limit impacts to existing uses, outreach process, future development of Youth Sports Complex.	Completed	May 12 & 19, 2014
RFP and selection process for design & engineering firms	Completed	April-June, 2014
Award of Contract to LPA, Inc, for outreach, planning, design, engineering, and site survey	Completed	February 2015
Community outreach & planning meetings held at Montague Park	In Progress	February & March, 2015
Council Study Session—Youth Soccer Park disposition. Referral & Guidelines to Ad Hoc Co	In Progress	June, 2015
Council approves CIP—Add \$5mm for construction; \$640K for YSP Field 3 conversion	Completed	June, 2015
Council Ad Hoc Committee Meeting	Pending	July 2015

For more information, please contact:
Parks & Recreation Department
City of Santa Clara
1500 Warburton Avenue
Santa Clara, CA 95050
(408) 615-2260
